

Update on Shooting Range Development in New Mexico





Cibola County Shooting Range



- May 8 – Contacted BLM to schedule cadastral survey
- May 20 – Presented MOU to County Commission
- May 28 – MOU Signed
- June 3 – Engineer meeting
- June 5 – Site visit with engineer
- June 8 – Established foot print for archaeology survey

NEXT STEPS: Complete surveys, property purchase and contract construction.

COMPLETION TARGET:
4-5 months



Cibola County Shooting Range
Project Area





Clovis Shooting Complex

- July 1, 2014 – Site visit with City of Clovis
- January 9 – Submitted project statement to FWS
- January 23 – Preliminary approval from FWS
- March 20 – Horizons of New Mexico accepted service to complete a conceptual design
- June 30 – Expected completion date for design

NEXT STEPS: Present design to City Commissioners for approval.

COMPLETION TARGET:

6-8 months





Youth Archery Range

Albuquerque Shooting Range Park




- March 4 – Provided city with revised MOU
- April 8 – Site visit with contractor and city
- April 22 – Meeting with contractor to review plans
- May 15 - Meeting with contractor to review plans and review estimate

NEXT STEPS: Complete MOU and contract construction.

COMPLETION TARGET:
4-5 months



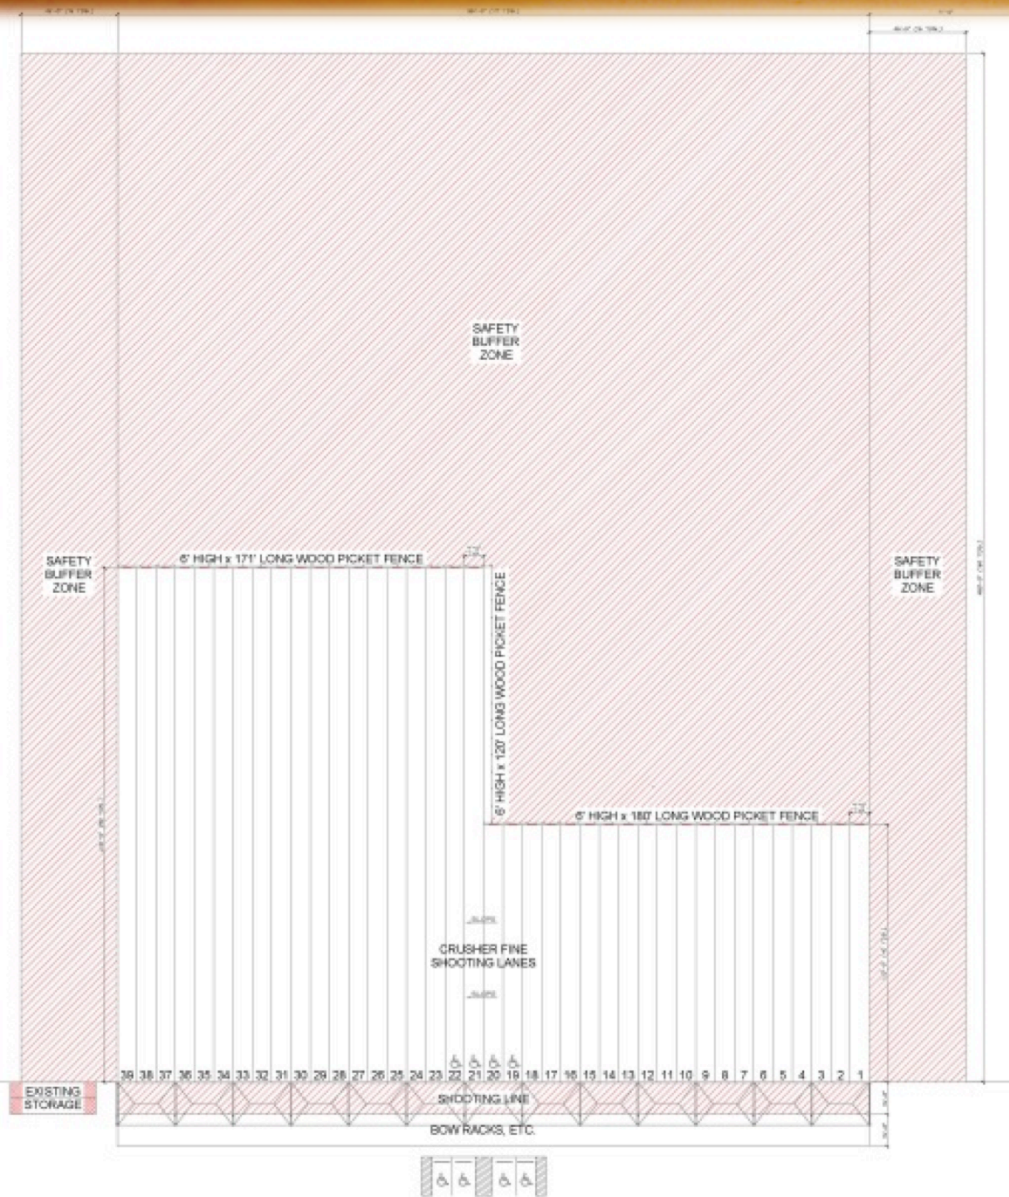


GENERAL NOTES

1. LEVEL AND COMPACT EXISTING EARTH WHERE SHOOTING LANES EXIST. APPROXIMATELY 80,640 SQUARE FEET OF EARTH TO BE COMPACTED AND LEVELED.
2. LAY COMPRESSIBLE FIBER BARRIER OVER COMPACTED EARTHEN BASE WITH 8" OF COMPACTED CRUSHER FINE, SLOPE 1/4" PER FOOT TO EAST END OF RANGE.
3. INSTALL 471 LINEAL FEET AT 6" HIGH, WOOD PICKET FENCE AT SOUTH END OF RANGE FOR SAFETY BUFFER.
4. INSTALL (13) 20'x27' CANOPIES.

ASSUMPTIONS:

1. 2 ARCHERS PER LANE



PROPOSED CANOPY

SCALE: 1/8"=1'-0"

Youth Archery Range

Albuquerque Shooting Range Park

PROPOSED ARCHERY RANGE
SCALE: 1"=30'-0"





Santa Fe Shooting Range



- February 7 – executed contract to complete R&PP
- May 5 – Preliminary meeting with contractor
- May 27 – Ordnance Survey conducted
- June 1-5 – Natural resource survey conducted
- June 8-19 – Cultural survey underway
- June 18 – Meet with design firm

NEXT STEPS: R&PP expected completion date - **April 29, 2016**

COMPLETION TARGET:
June 2016



