

Update on Shooting Range Development in New Mexico






Youth Archery Range

Albuquerque Shooting Range Park

- **June 30:** Invitation to Bid drafted
- Currently waiting for City of Albuquerque to return MOU

NEXT STEPS: Complete MOU and contract construction.

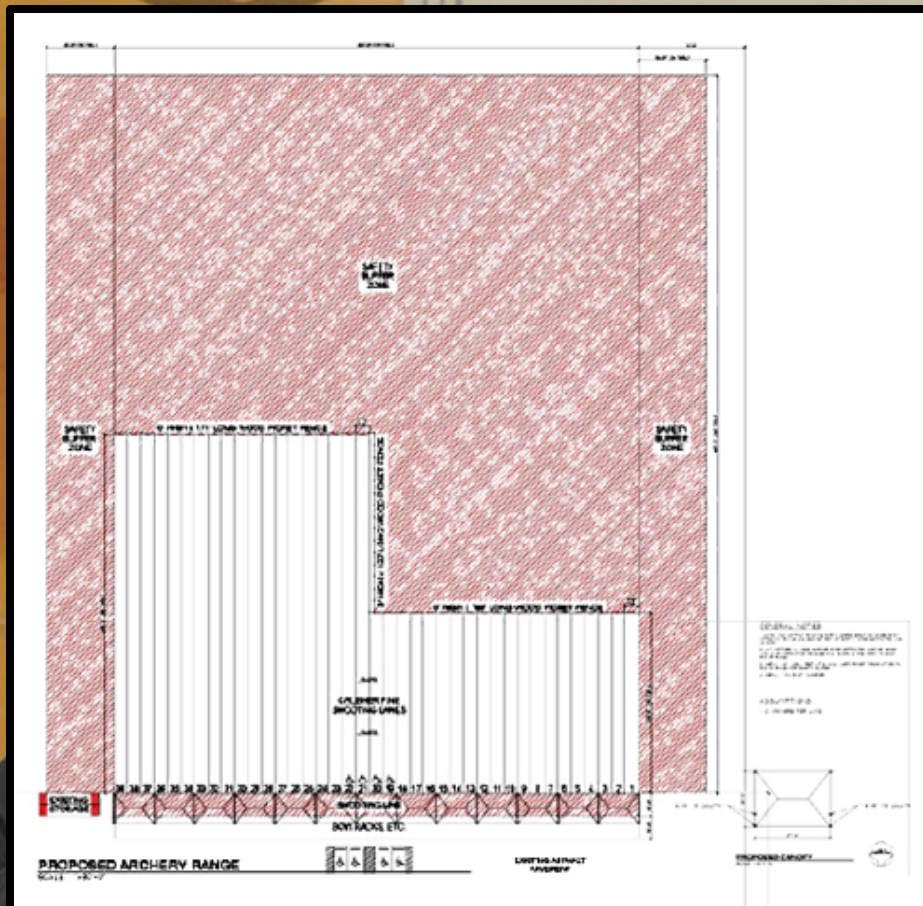

COMPLETION TARGET:
February 2016



Clovis Shooting Complex



- **Sept. 22:** Encumbrance approved for conceptual design
- **Oct. 30:** Expected completion date for design

NEXT STEPS: Present final design to City Commission for approval.

COMPLETION TARGET:
May 2016



Cibola County Shooting Range

- **July 16:** Met with BLM to review R&PP steps, responsibilities
- **Aug. 17:** Archaeology survey started, completed Sept. 1
- **Aug. 25:** BLM started process for Federal Register notice
- **Sept. 10:** Contacted grazing leasee with intent to purchase lease
- **Sept. 22:** Encumbrance approved for plan of development



NEXT STEPS: Complete archaeology survey report, Plan of Development, NEPA, Mineral survey, Federal Register published, Appraisal, Cadastral Survey, Construction

COMPLETION TARGET:
September 2016



FEDERAL TIMELINE

- **Sept. 4 - Sept 3, 2017:** Letter to current grazing permittee sent out to serve as two-year notification to reduce grazing acres.
- **Oct. 1:** Land Description Review by Cadastral Survey (required for Federal Register Notice)
- **Oct. 9:** Federal Register Notice review by State Office and Washington Office for review
- **Dec. 1:** Federal Register Notice published
- **Jan. 15, 2016:** Comment period ends provided Federal Register Notice is published on 12/1/15
- **Feb. 1, 2016:** End of Governor's review period. Classification of the land will become effective provided no adverse comments are received





FEDERAL TIMELINE

- **Feb. 15, 2016:** T & E Survey, Mineral Potential Report
- **Mar. 15, 2016:** Cadastral Survey
- **Apr. 1, 2016:** NEPA (Environmental Assessment)
- **May 15, 2016:** Environmental Site Assessment – 4-6 month process. Valid for 6 months.
- **May 30, 2016:** Appraisal – Valid for 12 months and will not be requested until the comment period is closed.
- **June 5, 2016:** Issue decision offering the applicant a lease with a limited reversionary provision and option to purchase
- **July 2016:** Construction Begins





Santa Fe Shooting Range

- **June 19:** Cultural survey completed
- **August 7:** Santa Fe County provided Lidar Survey data
- **August 17:** Biological Evaluation and Cultural Resources Inventory draft reports provided to NMDGF
- **August 26:** Coordinated with Santa Fe County for a range clean-up day, October 3



NEXT STEPS: R&PP expected completion date - **April 29, 2016**

COMPLETION TARGET:
September 2016

